

Overall Spatial Structure and Near-term Delivery

Use the rail heritage corridor as the framework, define three key districts and prioritise mobility continuity, service gaps and retrofit



NEAR-TERM PRIORITIES: MOBILITY PILOT, SERVICE NODES, GROUND-FLOOR RETROFIT, STATION LINKS

A 1 km mobility pilot, three first-stage nodes and three district projects establish a continuous public-space and service network.



PROGRAM REGISTER

11.41 km²

overall working base

3

key delivery districts

6

near-term projects

0- 0–24 mo

prop

NEAR-TERM CONTROLS

- 01 verify formal boundaries and tenure
- 02 review rail safety and utilities first
- 03 coordinate public and revenue uses
- 04 assign delivery, operations and maintenance

Key Delivery Districts and Near-term Projects

Each district receives its own project list, prerequisites, renewal method and delivery sequence



EXISTING-SPACE RETROFIT

Ground-floor access, barrier-free routes, stormwater and staffed service are delivered as one project.

KEY-DISTRICT PROJECT REGISTER

P-03 Zhongzhiyuan Validation District

192.1 ha / 192.9 ha

1.5 ha controlled validation field

tenure - safety review - traffic/fire

P-04 AI Origin Collaborative District

104.3 ha / 104.3 ha

3,000 m² shared ground floor

lease - structure/fire - operations

P-02 Dazhongsi Station-City District

72.0 ha / 72.0 ha

station-city public-hall interface

flow/evacuation - rail - tenure

Published and recalculated areas differ by less than 0.5%; official extents remain subject to statutory confirmation.

Project Review Requirements for Public AI Services

Review accountable owner, human service, data use, stop authority, complaints and annual evaluation for twelve proposed services



TWELVE PROPOSED SERVICES

SERVICE | LOCATION | OWNER TYPE | STAFFED ROUTE

S01	AI literacy room	Dazhongsi - named operating body	S02	Multilingual Jing-Zhang guide	corridor - named operating body
S03	Youth urban issues studio	AI Origin - named operating body	S04	Learning and career support	AI Origin - named operating body
S05	Intergenerational digital service desk	service nodes - named operating body	S06	Accessible-route co-mapping	corridor - named operating body
S07	Child-safe dialogue evaluation	Zhongzhiyuan - named operating body	S08	Low-speed robot route test	Zhongzhiyuan - named operating body
S09	Privacy-preserving learning tool test	AI Origin - named operating body	S10	Edge offline and energy test	Zhongzhiyuan - named operating body
S11	Facility maintenance training	Zhongzhiyuan - named operating body	S12	AI service notice and public feedback	3 districts - named operating body


APPLICATION REVIEW

- 01 owner + funding
- 02 staffed or physical route
- 03 necessary data + retention
- 04 personal-data protection
- 05 fault switching + emergency
- 06 stop + termination authority
- 07 fees, status + complaint notice
- 08 records + annual review



Planning Indicator Management and Acceptance

Nine indicators are assigned to base-map checks, design control and operating assessment with methods, owners and review cycles

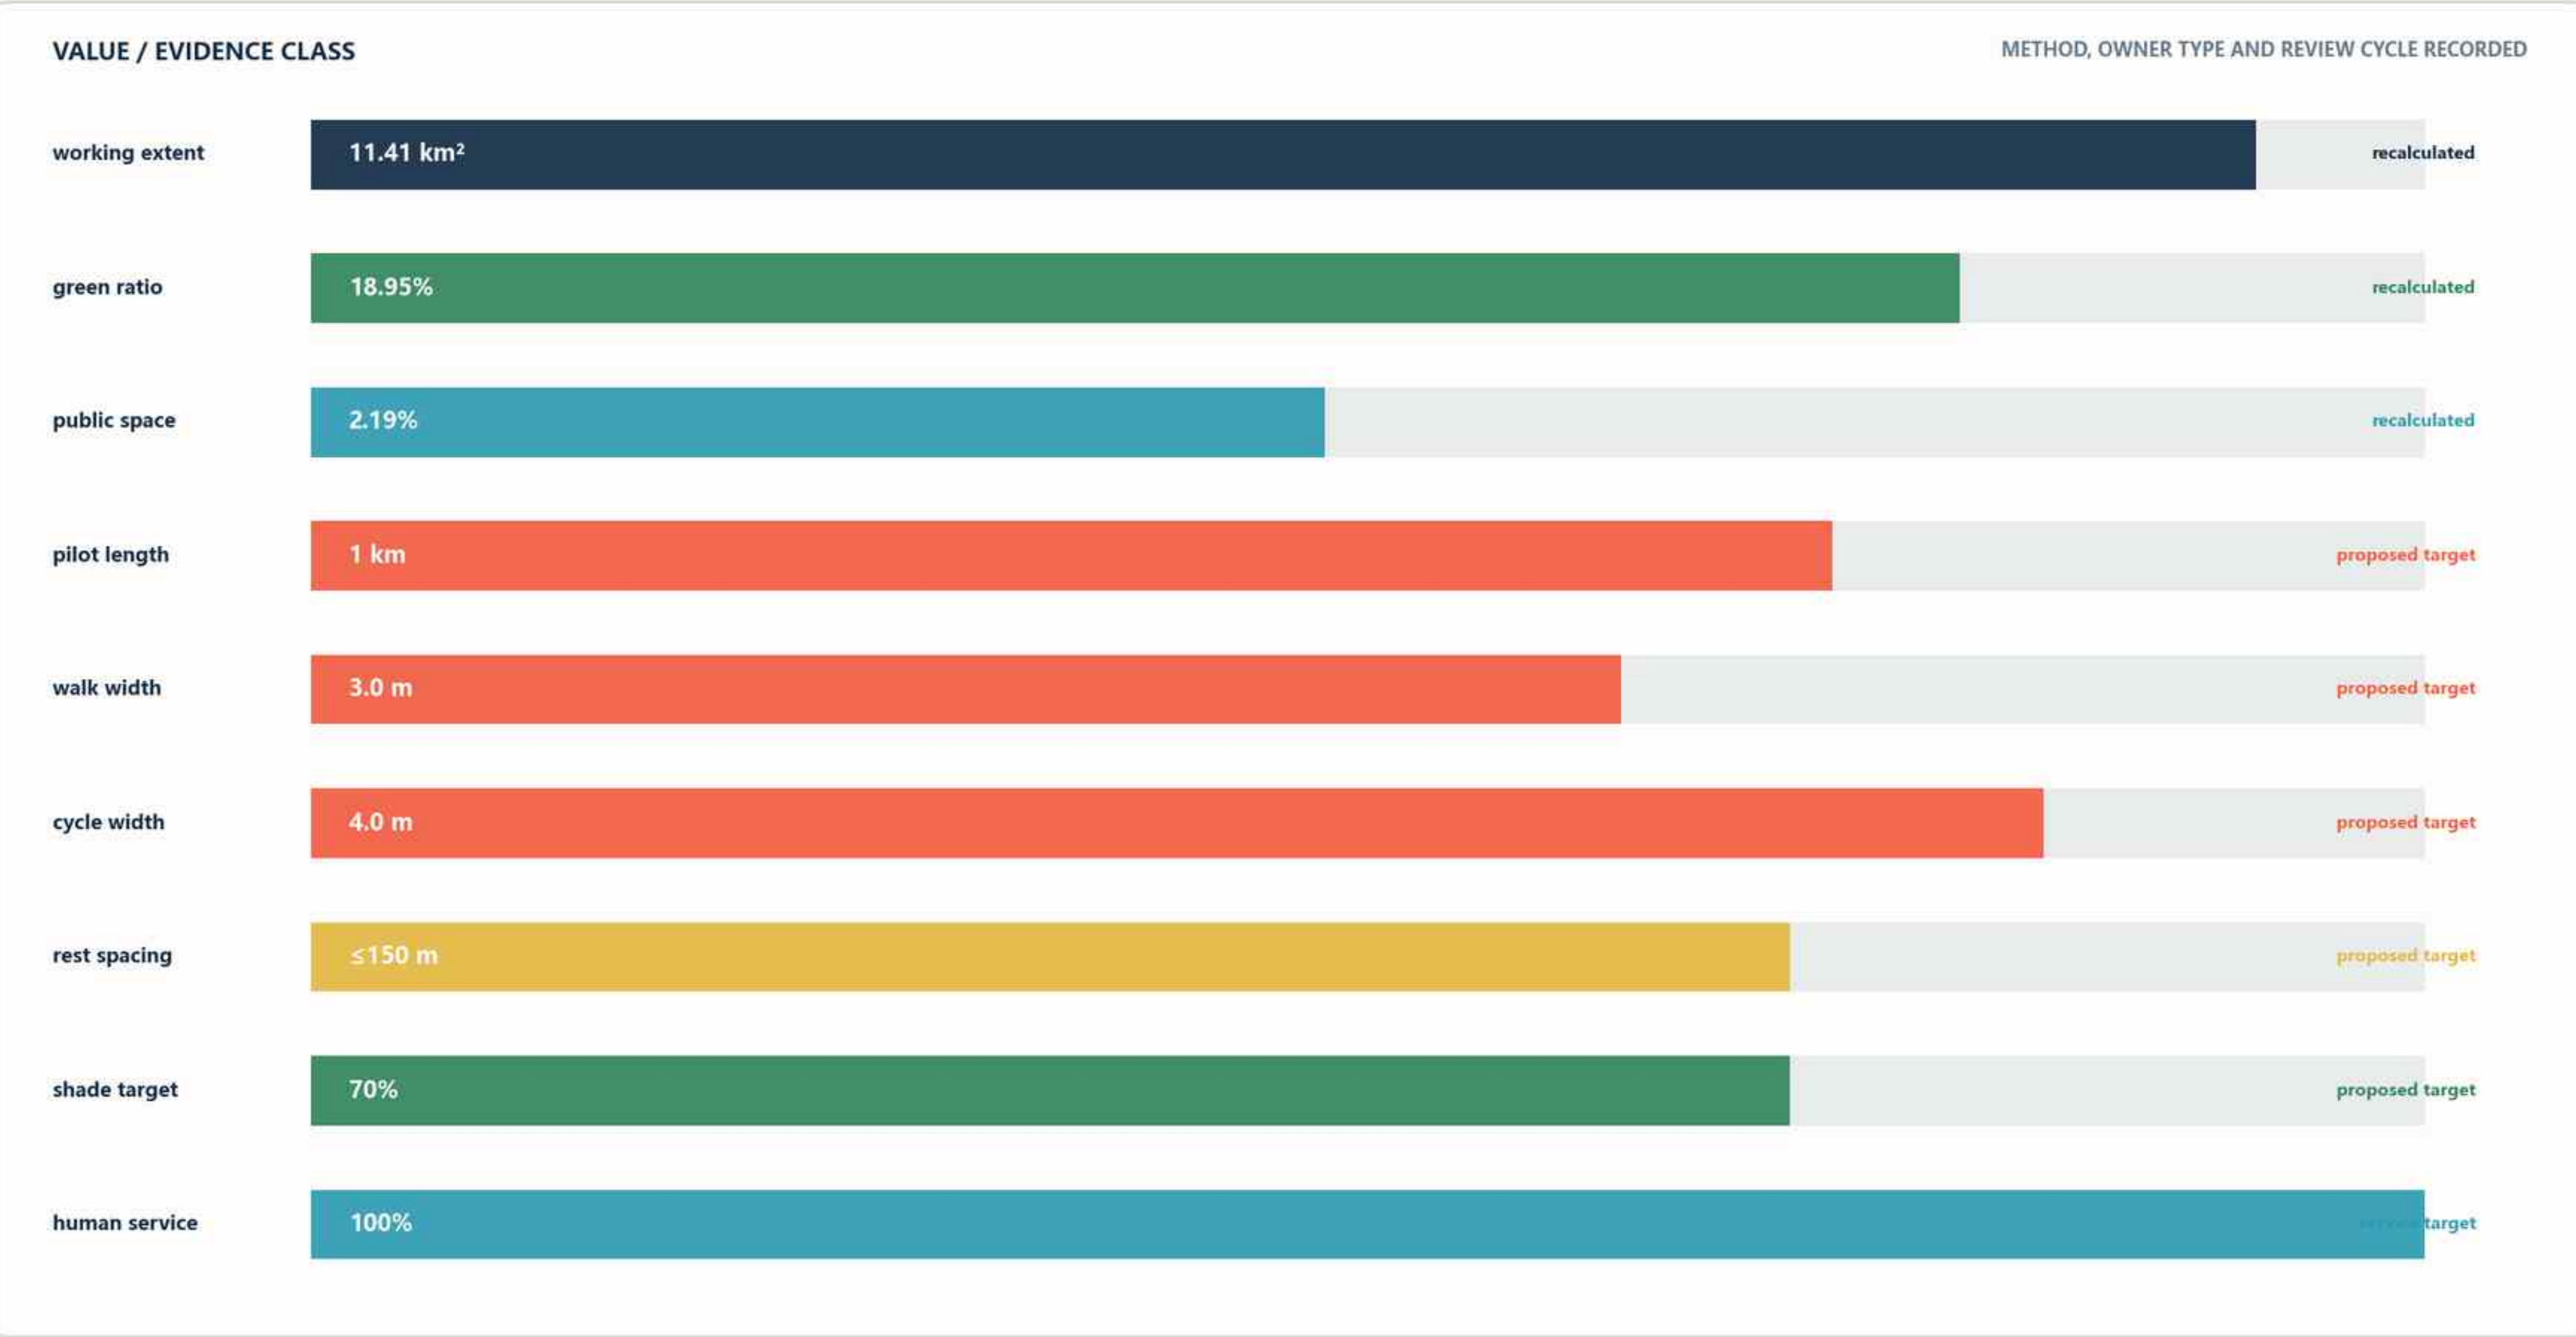

Functional Zoning, Area Balance and Renewal Method

Six renewal-unit types record area balance, retrofit, new uses, facility additions and delivery conditions



SIX RENEWAL UNITS WITH DEFINED TASKS AND DELIVERY CONDITIONS

The zones support project coordination; statutory use, intensity and compatibility are confirmed through implementation planning.

LAND + TASK REGISTER


LU-01	R&D + safety review
208.6 ha	- 18.3%
LU-02	talent housing + amenities
214.4 ha	- 18.8%
LU-03	training + technology transfer
204.9 ha	- 17.9%
LU-04	rail culture + public service
180.8 ha	- 15.8%
LU-05	digital service + commerce
166.2 ha	- 14.6%
LU-06	blue-green + utilities
166.4 ha	- 14.6%

1141.3 ha

working-base zone total

Near-term Mobility and Stormwater Delivery Requirements

Address mobility gaps, limited rest and fragmented drainage through coordinated walking, cycling, shade, stormwater and service stops

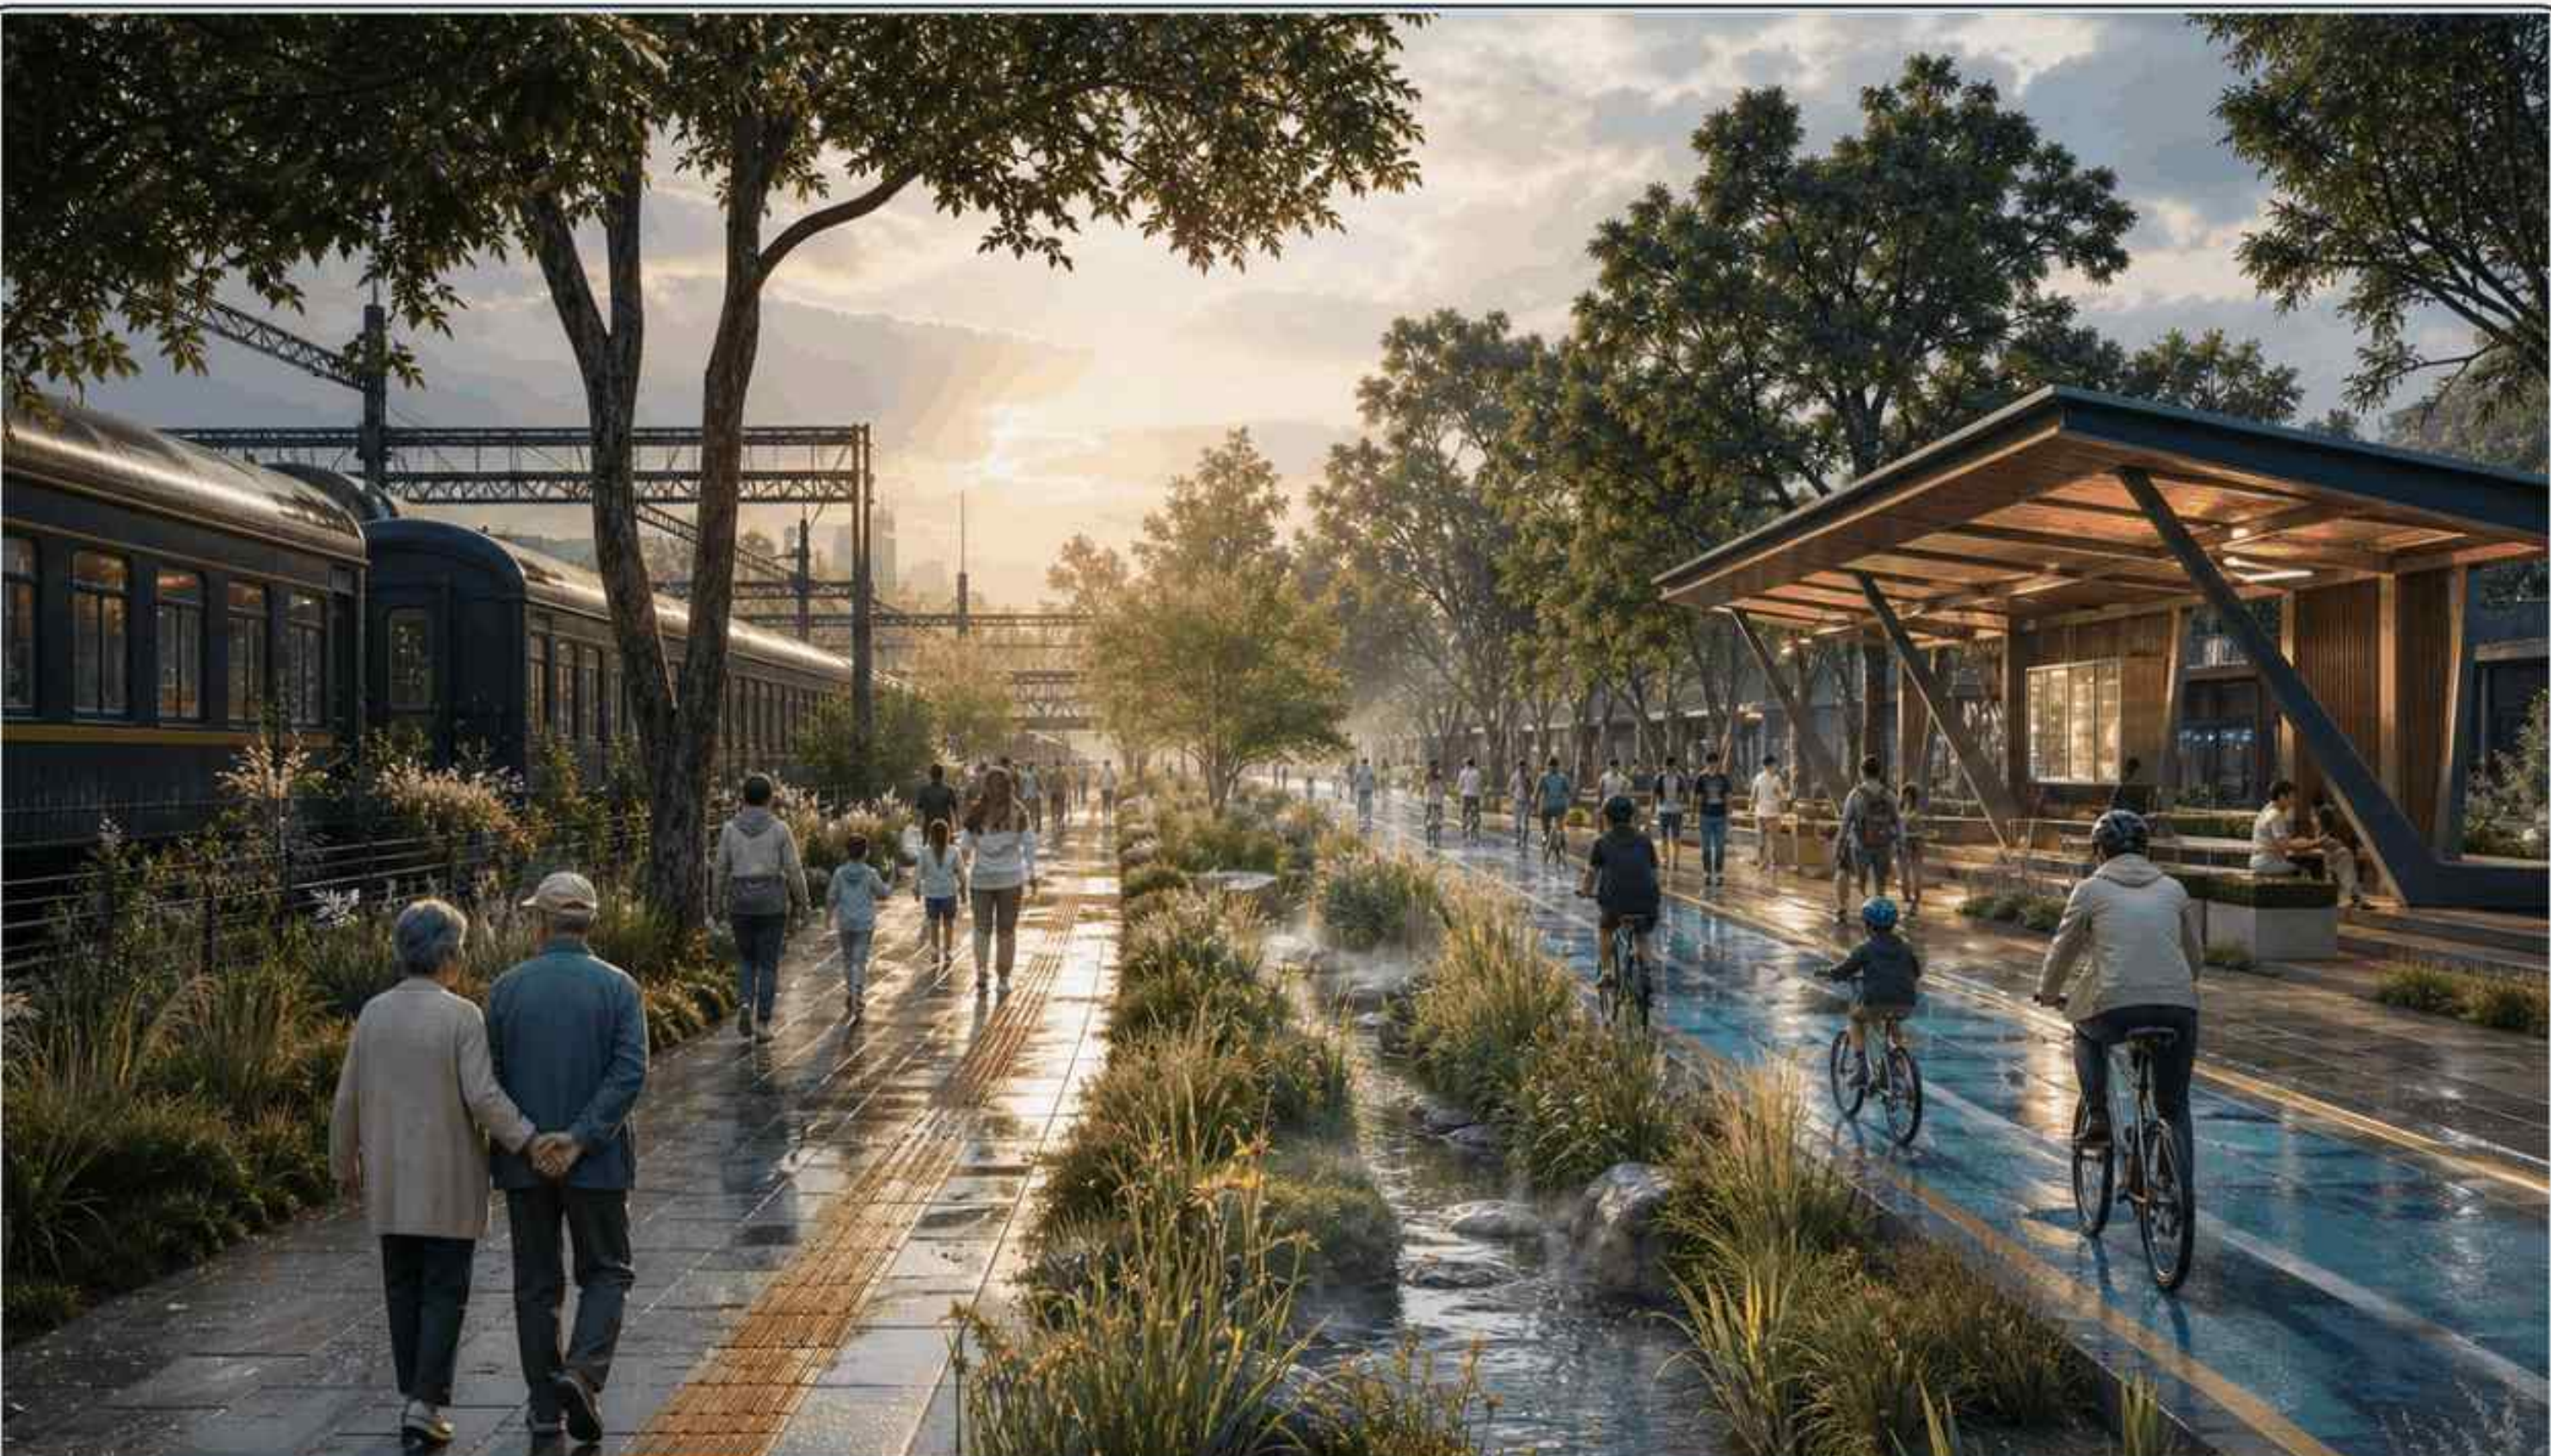

ILLUSTRATIVE COMPLETED VIEW OF THE MOBILITY PILOT

Walking, cycling, stormwater and service stops are coordinated within a 12 m typical section.

CLIMATE + SPATIAL RESPONSE

35.58°C

daily Tmax P95

22.3 d/y

days ≥35°C

649.1 mm

annual rain

4.05

daily solar

12 m FLEXIBLE EDGE



walk	rain	cycle	service
3.0 m	2.5 m	4.0 m	2.5 m

clear width · drainage · shade + rest

Priority-user Needs and Project Rectification List

Complete priority-user walk-throughs before initiation and record issues, rectification duties and responses

REGISTERED USER ISSUES 0-3

Children and families	3		2		3		
Older people and caregivers	1	3	3				1
Disabled users	3		1		1	2	
Long-term residents			1		3		1
Renters and small businesses	1		1	3	3		1
Students and young talent			3	3		1	
Commuters and visitors	3				1		
Frontline service and maintenance staff			1	2		1	3
Nearby campuses, parks and public institutions				1	2	1	
	mobility	rest + care	human service	learning + work	delivery burden	data + digital	maintenance + takeover

SURVEY + ACTION ARRANGEMENT

9类

priority-user groups

6项

participation steps

1套

rectification register

Coverage is calculated after population, employment and time-of-day flow baselines; current action follows group issue lists.

Near-term Project Register and Delivery Conditions

Six near-term projects record scope, prerequisites, funding, schedule, acceptance and operating responsibility

SIX NEAR-TERM PROJECT CARDS

SCOPE | OWNER TYPE | WINDOW | PREREQUISITES | OUTPUT

P-01 Jingzhang mobility pilot

SCOPE 1 km walking, cycling, stormwater and rest

OWNERS district · subdistrict · rightsholder

WINDOW 6-18 months | M

START 3 prerequisites

P-02 Dazhongsi station connection

SCOPE four-way access, wayfinding, service and parking

OWNERS subdistrict · station · transport · rightsholder

WINDOW 12-24 months | L

START 3 prerequisites

P-03 Zhongzhiyuan R&D test field

SCOPE 1.5 ha R&D test, safety buffer and training

OWNERS park · test bodies · safety evaluator

WINDOW 12-24 months | L

START 4 prerequisites

P-04 AI Origin shared ground floor

SCOPE 3,000 m² learning, talent and shared work

OWNERS rightsholder · subdistrict · campus/community · operator

WINDOW 9-18 months | M

START 3 prerequisites

P-05 public-service node prototype

SCOPE 320 m² staffed service, amenities and stormwater

OWNERS subdistrict · community · facility operator

WINDOW 6-12 months | M

START 4 prerequisites

P-06 public-AI management system

SCOPE applications, joint review, work orders and evaluation

OWNERS district · service operators · evaluator

WINDOW 3-9 months | S

START 4 prerequisites

FUNDING + OPERATIONS

01 PUBLIC SPACE + AMENITIES

capital plan names asset recipient and maintenance body

02 REVENUE + SHARED SPACE

rightsholder and operator cost retrofit, lease and staff

03 R&D TEST + DIGITAL SERVICE

implementer funds equipment, insurance, safety and upkeep

04 PRE-START FUNDING GATE

capital, annual O&M and staffing documented together

COST CLASS S <5m | M 5-20m | L 20-50m CNY

Typical-section Controls for the Jingzhang Pilot

A 12-m typical section addresses walking gaps, mixed traffic, limited rest and stormwater drainage



PILOT DELIVERY VIEW | accessible walk + rain garden + two-way cycling + human service

SECTION CONTROLS + ACCEPTANCE

12.0 m total | four continuous functional bands

- 01

WALKING

≥3.0 m

continuous clear width, tactile and kerb-ramp links

ACCEPT field width survey
- 02

STORMWATER

≥2.5 m

complete inflow, overflow and drainage route

ACCEPT hydraulic check + flow test
- 03

CYCLING

≥4.0 m

two-way operation with speed control at crossings

ACCEPT marking width + conflict review
- 04

SERVICE EDGE

≥2.5 m

seating, shade and staffed wayfinding

ACCEPT facility list + access audit

DELIVERY INTERFACES

- coordinate rail protection and maintenance access
- integrate street limits, utilities and existing trees
- retain physical wayfinding and human service during outages

Public-service Node Delivery and Operations Guide

A 320 m² prototype defines site, program, staffing, utilities, acceptance and exit requirements



NODE AXONOMETRIC INTENT | 20 m × 16 m | continuous accessible loop

NODE DELIVERY + OPERATIONS

250–400 m² program range | 320 m² prototype

- 01

FOOTPRINT

320 m²

20 m × 16 m prototype with demountable components

ACCEPT site and built-area check
- 02

HUMAN SERVICE

24–36 m²

counter, waiting, storage and staffed position

ACCEPT hours and staffing roster
- 03

MICROCLIMATE

≥70%

continuous shade across principal stay areas

ACCEPT summer solar study + field audit
- 04

RESPONSE

60 s / 24 h

human acknowledgement and routine fault logging

ACCEPT monthly response + work-order log

HANDOVER + EXIT MANAGEMENT

- joint utilities, fire, access and site-permit review
- facility list, duty register and monthly inspection record
- remove equipment if operations lapse; retain basic civic amenities

Regional Annual Action Programme


Five collaboration units specify exchange, annual action, owner types and receipts

UNIT	ROLE	RESOURCE EXCHANGE	ANNUAL ACTION	RECEIPT
Beimei Community	neighbourhood co-test	public needs, research, devices, methods and service feedback	4 walks + 6 service improvements	issues + corrections
Future Science City	research scenario validation	public needs, research, devices, methods and service feedback	2 joint scenario challenges	challenge + test report
Huaiyou Science City	science-to-city translation	public needs, research, devices, methods and service feedback	2 course packs + 1 urban validation	course + feedback
Beijing E-Town	robotics and manufacturing validation	public needs, research, devices, methods and service feedback	3 device tests + 1 supply-chain session	safety + conversion
Beijing-Tianjin-Hebei	interregional scenario network	public needs, research, devices, methods and service feedback	1 catalogue + 2 roadshows + 3 off-site validations	catalogue + validation

DELIVERY RULE: enter the programme after annual agreement; register provenance, rights, budget, owner and exit.

Benchmark Cases and AI Innovation Ecosystem

Six comparisons set policy choices; four stages and eight factors govern annual delivery

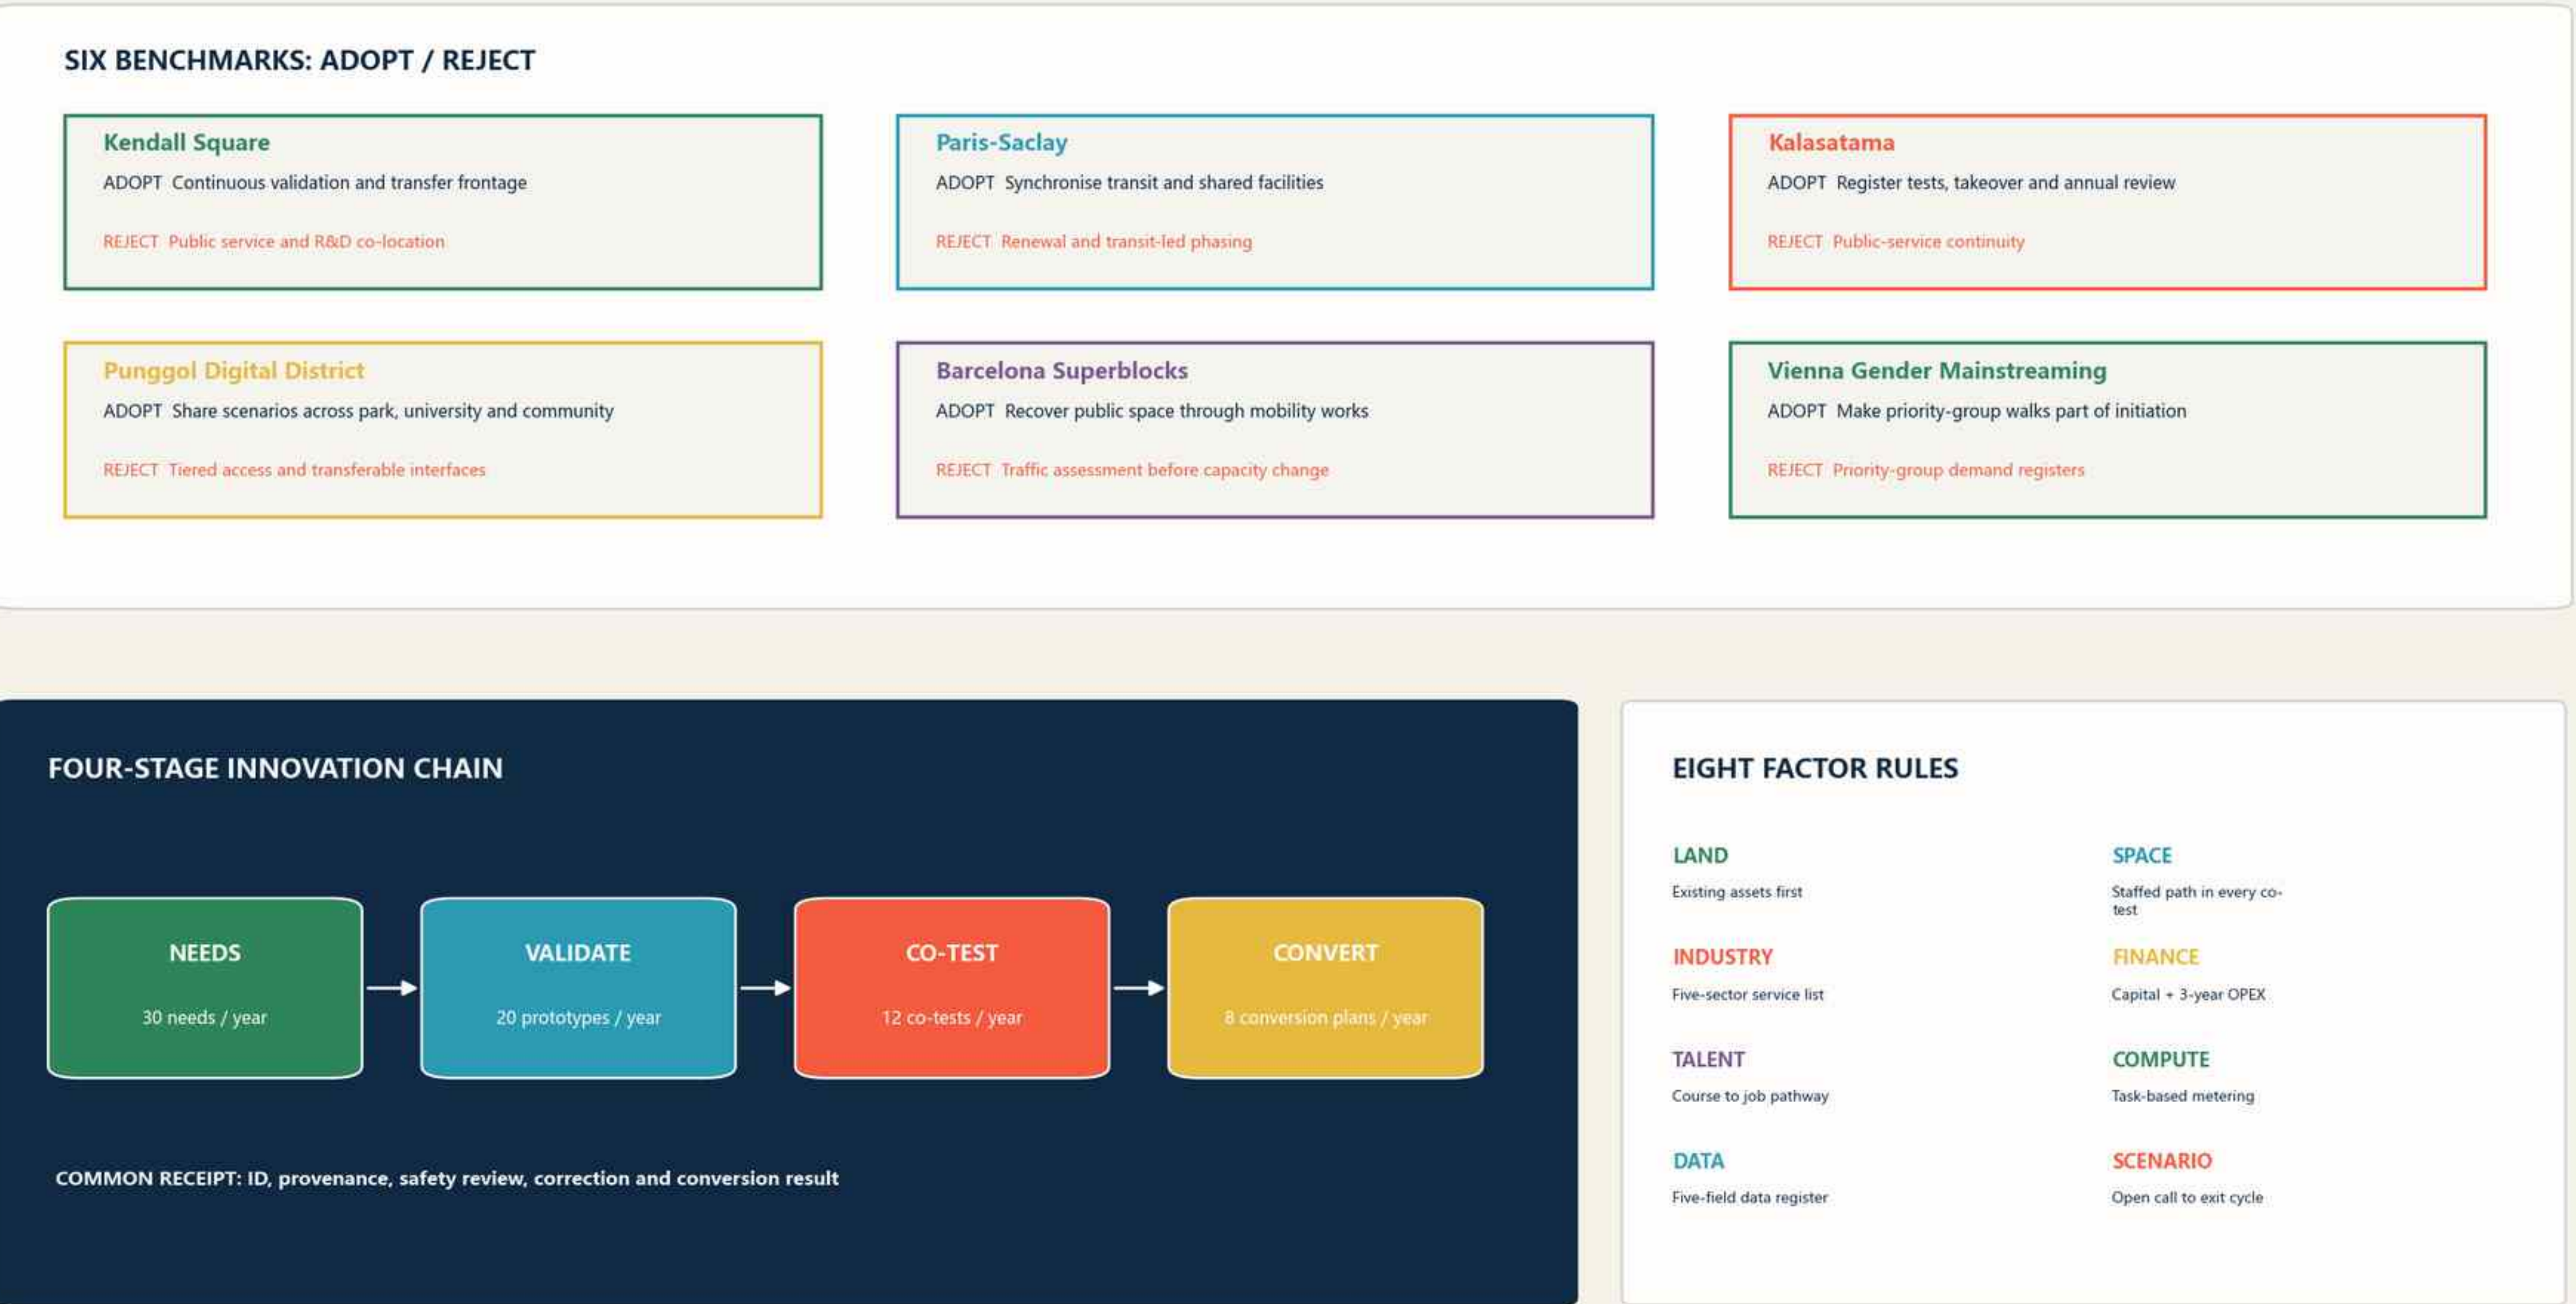

Cultural Narrative, Civic Landmarks and Recognition

Three narratives become everyday civic facilities; contributions receive annual review

THREE CIVIC NARRATIVES

INDEPENDENT ENGINEERING

1909—1949

Rail engineering, survey and construction archive

OPEN INNOVATION

1980—2025

Zhongguancun research, open source and transfer

CIVIC INTELLIGENCE

2026—

Rights, duties and rules for AI public service

THREE CIVIC LANDMARKS

L-01

ORIGIN MILESTONE COURT

1909 / 1980 / 2026 archive and courses

AI Origin Community

1 oral-history set + 1 course / year

L-02

OPEN MODEL GALLERY

Models, methods, failure cases and stop records

Zhongzhiyuan

20 validation records / year

L-03

CIVIC GOVERNANCE SIGNAL TOWER

Live status for twelve public AI services

Dazhongsi Public Hall

live status + annual public report

OPEN CONTRIBUTION ARCHIVE

problem discovery

open tools + data

safety + accessibility

long-term maintenance

AWARD RULE

Public output, co-authorship and verifiable record; sponsorship alone does not qualify.

Annual Events, Developer Community and Conversion

Four seasons, four working groups and a five-gate pathway share one annual programme

FOUR-SEASON ACTION CALENDAR

SPRING

URBAN PROBLEM SEASON

30 needs + 6 site walks

scenario register

SUMMER

OPEN VALIDATION SEASON

20 prototypes + 8 negative tests

test + correction records

AUTUMN

CIVIC INTELLIGENCE WEEK

12 co-tests + 4 workshops

co-test + open output catalogue

WINTER

ANNUAL GOVERNANCE ASSEMBLY

12 services + 6 packages reviewed

continue / correct / reduce / stop list

FOUR DEVELOPER WORKING GROUPS

01

public service + accessibility

02

model safety + evaluation

03

edge devices + robotics

04

urban data + maintenance

ANNUAL: 12 open workdays and 8 reusable outputs

FIVE-GATE CONVERSION PATHWAY

REGISTER

VALIDATE

CO-TEST

PROCURE

SCALE

NEXT GATE: rights clear, cost affordable, owner assigned and correction closed.

Events, site maintenance and staffed service use separate budgets.

Planning Basis and Material-use Statement

Materials are classified, sourced, managed by use and reviewed as an updatable planning record

8

MATERIAL CLASSES

30

PLANNING FIGURES

4

PDF DELIVERABLES

2

LANGUAGE SETS

MATERIAL	SOURCE / RIGHT	PLANNING USE	MANAGEMENT REQUIREMENT	STATUS
proposal text and translations	agent-authored for this submission	original submission text	policy and standard summaries remain attributed	REGISTERED
technical figures and diagrams	generated locally from submission data by the package build script.	agent-authored graphics	provisional geometry is labelled and cannot be treated as statutory mapping	REPRODUCIBLE
OpenStreetMap context	OpenStreetMap contributors	ODBL 1.0 attribution	background context only; no ownership or statutory inference	LICENSED
NASA POWER climate baseline	NASA POWER daily API documentation and retrieved values	public scientific data with attribution	concept-stage point-grid baseline; engineering design requires local data	REGISTERED
Blender corridor rendering	agent-generated from conceptual massing	agent-authored rendering	not an as-built or surveyed model	CONCEPT
generated concept scenes	OpenAI image generation directed for this submission	submission concept imagery	design intent only; no identifiable real people or official endorsement	ILLUSTRATIVE
Three.js offline viewer	Three.js 0.185.1 bundled locally	MIT license	license notice retained in source package	LICENSED
system fonts	Microsoft 'Yale' or available CJK system font	render-only local font use	font files are not redistributed	EMBEDDED

STATUTORY BASIS

Policies, standards and task sources are indexed in the source register

TECHNICAL BASE

The working base is updated with official boundaries, survey and current-condition records

DELIVERABLE USE

Concept visuals convey planning intent; delivery proceeds through specialist design outputs

Public-space Identity and Wayfinding Guidelines

A three-level system coordinates corridor gateways, direction signs and service confirmation

HIERARCHY + APPLICATION

A continuous, legible and all-age public-information system

L1 | CORRIDOR GATEWAY

At district entrances and station-city interfaces, show identity and overall direction.

L2 | DIRECTION SIGN

At route decisions; show destination, distance, accessible route and interchange.

L3 | SERVICE CONFIRMATION

At service nodes; show hours, human desk, status and feedback route.

INFORMATION + MAINTENANCE

Separate project identity from government emblems and maintain a clear information boundary

Every AI service point includes a human-service sign and non-digital access instructions

Coral marks duty, service status and stop information; navy and cyan support routine navigation

Inspect monthly; create and publish a routine-fault work order within 24 hours

GROW WITH JINGZHANG

RAIL GATEWAY · WAYFINDING · HUMAN SERVICE · NIGHT IDENTITY
